

**TASDEEQ – DIGITAL VERIFICATION PLATFORM
TASDEEQ-V1**

Project Management Plan

Contents

1. Background and References	3
1.2 The Client	3
1.3 Expected Goals.....	3
1.3.1 Technical Goals.....	3
1.3.2 Economical Goals	3
1.3.3 Strategic Goals	3
1.4 Project Classification	3
1.5 Reference Contract Documents	4
2. Project Structuring	4
2.1 OBS (Organizational Breakdown Structure)	4
2.2 ABS (Activity Breakdown Structure).....	5
2.3 PBS (Product Breakdown Structure).....	5
2.4 WBS (Work Breakdown Structure).....	6
2.5 Procurement Plan	7
2.6 Measurement and Control Methodologies	7
2.7 Reporting.....	7
3. Supporting Managerial Activities	7
3.1 Risk Management	7
3.2 Quality Management.....	8
3.3 Development	8
3.4 Configuration Management	8
3.5 Acceptance Criteria / Testing.....	8
3.6 Phase Reviews.....	8
4. Master Plan	8
4.1 Contract Plan.....	8
4.2 Master Plan and Associated Milestones	8
5. Technical Budget.....	9
5.1 Costs / Revenues / Margins	9
5.2 Business Plan	9
5.3 External Costs Plan	9
5.4 Billing and Collections	9
5.5 EVA Analysis	10

1. Background and References

1.1 Objective

The objective of the Tasdeeq Digital Verification Platform project is to design and deploy a secure, scalable digital verification system for the Italian and European market.

The platform will enable organizations to perform identity, credential, and background verification in a compliant, efficient, and reliable manner, fully aligned with GDPR and Italian data protection regulations.

1.2 The Client

The client is **Tasdeeq**, a digital verification service provider operating in the **Italy / EU region**, focusing on delivering secure and compliant verification solutions to enterprises such as banks, fintech companies, employers, telecom operators, and public institutions.

1.3 Expected Goals

1.3.1 Technical Goals

The technical goal is to develop a highly secure, scalable, and API-driven verification platform, ensuring:

- High system availability
- Strong data security and encryption
- Seamless integration with third-party systems
- High performance and reliability

1.3.2 Economical Goals

The economic goal is to optimize development and operational costs while maintaining quality, and to achieve a positive return on investment through enterprise contracts and service-based revenue within the initial operational period.

1.3.3 Strategic Goals

The strategic goal is to strengthen Tasdeeq's position in the digital identity and verification market by offering a compliant, trusted, and enterprise-grade solution, increasing adoption across Italian and EU-based organizations.

1.4 Project Classification

The project is classified as the development and deployment of an enterprise IT system.

The scope of the project is regional (Italy / EU), with a focus on regulated industries requiring secure digital verification services.

1.5 Reference Contract Documents

The reference documents for the project include:


- Statement of Work (SOW)
- Project Proposal
- Project Management Plan
- Contract Agreement
- Non-Disclosure Agreement (NDA)
- Technical Specifications
- User and System Documentation

2. Project Structuring

2.1 OBS (Organizational Breakdown Structure)


The OBS defines the organizational structure and responsibilities involved in the Tasdeeq project, including:

- Project Manager
- Backend Development Team
- Frontend Development Team
- Quality Assurance Team
- Support Team

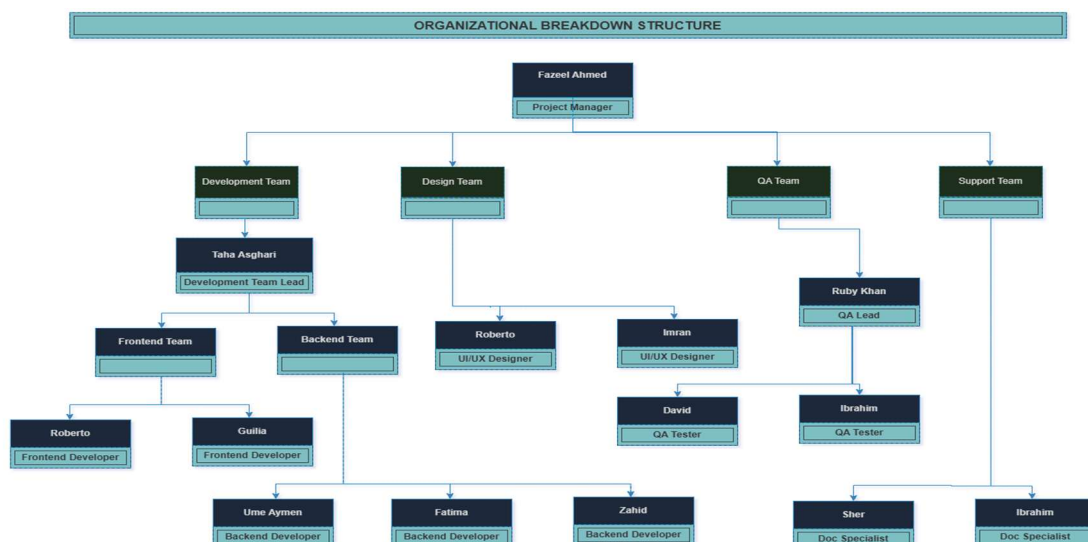

2.2 ABS (Activity Breakdown Structure)


The ABS identifies and organizes all activities required to complete the project, covering planning, analysis, design, development, testing, deployment, and documentation.

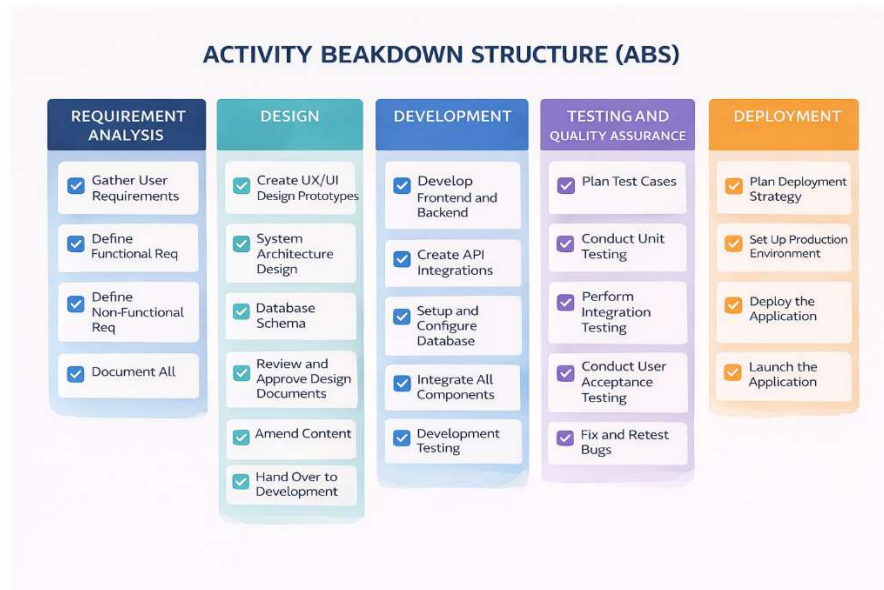

2.3 PBS (Product Breakdown Structure)

The PBS defines the main components of the product, including:

- Identity Verification Module
- Credential & Background Verification Module
- API Gateway
- Audit and Logging Module

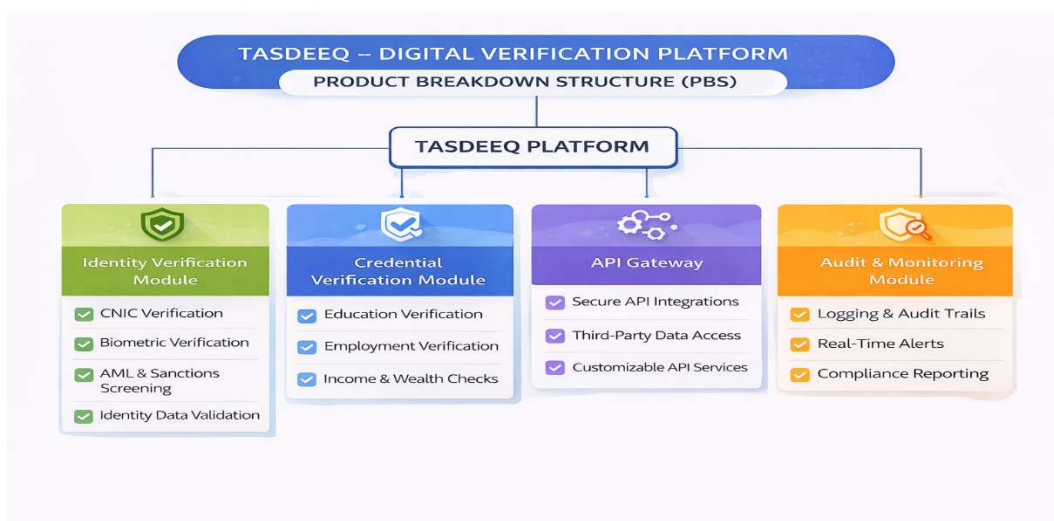

2.4 WBS (Work Breakdown Structure)

The project is divided into the following work packages:

WBS (Task)	Name
TASDEEQ_V1	Tasdeeq Digital Verification Platform
WP1	Project Management
WP1.1	<i>Project Planning</i>
WP1.2	<i>Project Monitoring & Control</i>
WP1.3	<i>Project Closure</i>
WP2	Requirements Analysis
WP2.1	<i>Requirements Gathering</i>
WP2.2	<i>Functional Requirements Definition</i>
WP2.3	<i>Non-Functional Requirements Definition</i>
WP2.4	<i>Requirements Documentation</i>
WP3	Design
WP3.1	<i>System Architecture Design</i>
WP3.2	<i>API Design</i>
WP3.3	<i>Database Design</i>
WP3.4	<i>Security & Compliance Design</i>
WP3.5	<i>Design Review and Approval</i>
WP4	Development
WP4.1	<i>Backend Development</i>
WP4.2	<i>API Development</i>
WP4.3	<i>Integration</i>
WP4.4	<i>Development Testing</i>
WP5	Quality Assurance
WP5.1	<i>Test Planning</i>
WP5.2	<i>Unit Testing</i>
WP5.3	<i>Integration Testing</i>
WP5.4	<i>User Acceptance Testing</i>
WP5.5	<i>Bug Fixing</i>
WP6	Deployment
WP6.1	<i>Deployment Planning</i>
WP6.2	<i>Production Environment Setup</i>
WP6.3	<i>Platform Deployment</i>
WP6.4	<i>Post-Deployment Testing</i>
WP7	Documentation
WP7.1	<i>Technical and User Documentation</i>

2.5 Procurement Plan

No major procurement activities are required for the Tasdeeq project, as development tools, licenses, and infrastructure are primarily available internally. External services may be used selectively for compliance audits or security assessments if required.

2.6 Measurement and Control Methodologies

The following tools and metrics will be used:

- Microsoft Project for scheduling (Gantt charts)
- Bug tracking tools for issue management
- Git for version control

Key performance indicators include:

- Defect density
- Verification success rate
- API availability
- Sprint velocity

2.7 Reporting

Weekly project status reports will be shared with stakeholders, covering progress, upcoming activities, risks, and issues, ensuring transparency and effective communication throughout the project lifecycle.

3. Supporting Managerial Activities

3.1 Risk Management

The project team will identify, assess, and mitigate project risks throughout the project life-cycle. Below table specifies the risk types along with the impact and exposure

Risk Table

Risk Type	Risk Description	Probability (1-3)	Impact				Risk Exposure	
			Time (1-3)	Costs (1-3)	Performance (1-3)		Technical	Management
Schedule Delays	Delays due to dependencies and resource issues	2	2	2	3	2	2	2
Technical Issues	Compatibility and technology limitations	3	2	2	2	2	3	2
Security Breaches	Data breaches and cybersecurity risks	1	3	1	2	2	3	1
User Adoption	Low user uptake and engagement	2	1	1	2	1	1	2

3.2 Quality Management

A structured quality plan will ensure that all deliverables meet defined standards. Rigorous testing will be conducted before acceptance and deployment.

3.3 Development

The development process will follow a structured and iterative approach, ensuring alignment with requirements and timely delivery of functional components.

3.4 Configuration Management

All system configurations, code versions, and deployment environments will be managed using standardized configuration management practices.

3.5 Acceptance Criteria / Testing

Clear acceptance criteria will be defined, and comprehensive testing will be conducted to ensure system reliability, security, and compliance.

3.6 Phase Reviews

Formal phase reviews will be conducted at the end of each major phase to validate deliverables before proceeding.

4. Master Plan

4.1 Contract Plan

A formal contract will be signed between the client and the project team, defining scope, responsibilities, timeline, and financial terms.


4.2 Master Plan and Associated Milestones

The Tasdeeq Project Plan defines the overall timeline and interdependencies of key project phases, from system design through deployment, ensuring a coordinated and controlled development process. The plan identifies critical milestones such as the completion of requirements analysis, system development, integration, testing, and final deployment, providing a structured framework to successfully achieve the project objectives within the approved schedule.

The Tasdeeq project is planned for the 2026–2027 period, with major milestones including:

- Requirements & Planning Completion: April 2026
- Design Phase Completion: August 2026
- Development Phase Completion: January 2027
- Integration & Testing Completion: March 2027

- Deployment & Launch: May 2027

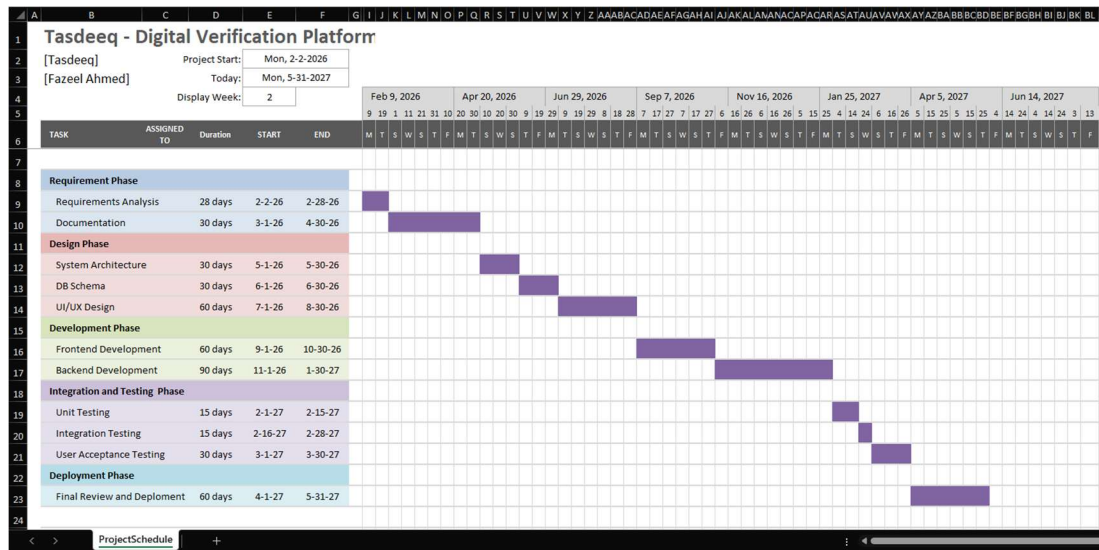

5. Technical Budget

5.1 Costs / Revenues / Margins

- **Development Cost:** €130,000
- **Total Project Value:** €180,000

5.2 Business Plan

The project aims to deliver a high-quality verification platform within the approved budget while monitoring CPI and SPI to ensure cost and schedule control.

5.3 External Costs Plan

External costs may include legal, compliance, and security audit services. All external expenses will be closely monitored to ensure budget adherence.

5.4 Billing and Collections

Payments are divided into four stages:

- 20% upon contract signing.
- 20% upon completion of design phase
- 30% upon completion of development phase
- 30% upon final deployment and launch

5.5 EVA Analysis

Revenue / Total Cost	= €180,000
Development Cost	= €130,000
EBIT	= €50,000
Estimated Tax	= €12,500
Net Income	= €37,500
